

Monthly Progress Report

Mukhyamantri Udyamshala
Yojana

August 2026



Private & Confidential

Contents

1. Progress in Mukhyamantri Udyamshala Yojana (MUY)

2. Quantitative Progress - Plan vs Achievements

3. District-wise Progress

4. Program Workstream Progress

5. Field Highlights

6. Report Basis and Data Notes

1. Progress in Mukhyamantri Udyamshala Yojana (MUY)

This Monthly Progress Report presents MIS-recorded progress for August 2026. Targets and achievements follow the approved MUY deliverables matrix for FY 2026-27.

909 CFA applications	0 Incubatees onboarded	26 Indicators reporting progress
--------------------------------	----------------------------------	--

Key monthly highlights

Call for Application: 909 achieved against a monthly target of 1,470.

Participants in Awareness cum Outreach activities: 574 achieved against a monthly target of 910.

Incubatees taken Part in Business Modules Training: 212 achieved against a monthly target of 700.

Business Model Canvas: 185 achieved against a monthly target of 600.

Business Registration: 74 achieved against a monthly target of 600.

Schematic Convergence: 48 achieved against a monthly target of 300.

Specialized Mentorship Support: 25 achieved against a monthly target of 65.

No. of Awareness cum Outreach activities for SHG members/Potential Lakhpati Didis/ SHGs/CBOs etc.: 24 achieved against a monthly target of 122.

2. Quantitative Progress - Plan vs Achievements

The table below presents the approved monthly target and MIS-recorded achievement for August 2026.

S.No.	Indicator	Type of Indicator	Target	Achievement	Achievement (%)
1	Outreach and Mobilisation				
1.1	Call for Application	Key Indicator	1,470	909	62%
1.2	District Level Workshops	Key Indicator	—	3	—
1.3	No. of Awareness cum Outreach activities for SHG members/Potential Lakhpati Didis/ SHGs/CBOs etc.	Non-Key	122	24	20%
1.3.1	Participants in Awareness cum Outreach activities	Non-Key	910	574	63%
1.4	EAP/EDP Sessions	Key Indicator	13	12	92%
1.5	Outreach through Community Organizations	Non-Key	4	0	0%
2	Identification and Onboarding of Enterprises				
2.1	Incubatees Onboarded	Key Indicator	700	0	0%
2.1.1	Onboarding of Potential Lakhpati Didi/ SHG Members/ CBOs*	Key Indicator	300	0	0%
3	Training & Capacity Building				
3.1	Business Skills Training Sessions	Key Indicator	39	7	18%
3.2	Incubatees taken Part in Business Modules Training	Non-Key	700	212	30%
3.3	Technical Trainings to Incubatees	Non-Key	1	0	0%
3.3.1	Technical Trainings to Potential Lakhpati Didis/ SHG Members/ CBOs	Non-Key	(Need Based)	1	—
3.4	Capacity Building of stakeholders (REAP, USRLM, Other Line department staff)	Key Indicator	0	0	—
4	Business Formalization				
4.1	Business Registration				
4.1.1	Business Registration	Key Indicator	600	74	12%
4.2	Legal & Licensing Support				
4.2.1	Artisan Card	Key Indicator	26	8	31%
4.2.2	FSSAI	Non-Key	75	14	19%
4.2.3	UTDB	Non-Key	20	1	5%
4.2.4	GST Registration	Non-Key	35	4	11%
4.2.5	Trademark application filling	Non-Key	0	1	—
4.2.6	GI Seller Registration	Non-Key	—	0	—
4.2.7	Advance Licensing Support (Mandi Licensing, Lab Test etc.)	Non-Key	(Need Based)	1	—
5	Mentorship				
5.1	Specialized Mentorship Support	Key Indicator	65	25	38%
5.2	Mentorship Support through online portal	Non-Key	0	0	—
6	Partnership & Forward Linkages				

S.No.	Indicator	Type of Indicator	Target	Achievement	Achievement (%)
6.1	No of Partners outreach	Non-Key	10	11	110%
6.2	Marketing Partners Onboarded through (LoA/Lol/MoU)	Non-Key	10	0	0%
6.3	Incubatees linked to online/offline Market	Key Indicator	150	15	10%
7	Business Acceleration Services				
7.1	No of Partners outreach	Non-Key	2	0	0%
7.2	Initiation of acceleration and co-incubation services	Key Indicator	150	15	10%
8	Funding & Schematic Convergence				
8.1	Schematic Convergence	Key Indicator	300	48	16%
8.2	Support to MUY Incubatee through Reap	Key Indicator	50	4	8%
8.3	Incubatees Pitch Deck Preparation	Key Indicator	20	0	0%
8.4	Demo Days	Key Indicator	1	0	0%
8.5	No of Partners outreach	Non-Key	5	0	0%
9	Other Support Services				
9.1	Business Model Canvas	Key Indicator	600	185	31%
9.2	Other Support Services - Labelling, Packaging, Logo Designing etc.	Non-Key	0	2	—
10	Branding, Communication & Knowledge Management				
10.1	Social Media Post	Key Indicator	10	3	30%
10.2	Preparation of Case Studies and Testimonials	Key Indicator	10	1	10%
10.3	MUY Newsletter	Key Indicator	—	0	—
10.4	IEC & Promotional Activities for MUY	Non-Key	1	0	0%
10.5	Buyer-Seller Meet	Key Indicator	0	0	—
10.6	Events/ Seminars/ Workshops	Key Indicator	0	0	—
11	Product Development				
11.1	Identification and Submission of Proposal for New Product Development	Key Indicator	0	0	—
12	Synergies Across Line Departments				
12.1	Stakeholder Consultation Workshop	Key Indicator	0	0	—
12.2	Meeting of staff with Line Department at Spoke/Hub/State Level	Non-Key	5	1	20%

The above-mentioned progress is based on the IT/MIS system developed under the Mukhyamantri Udyamshala Yojana and the applicable maker-checker approval workflow.

3. District-wise Progress

District-wise CFA and onboarding achievements recorded during the selected month.

S.N.	District	CFA applications	Incubatees onboarded
1	Almora	42	0
2	Bageshwar	2	0
3	Chamoli	114	0
4	Champawat	61	0
5	Dehradun	97	0
6	Haridwar	106	0
7	Nainital	158	0
8	Pauri Garhwal	114	0
9	Pithoragarh	101	0
10	Rudraprayag	20	0
11	Tehri Garhwal	20	0
12	Udham Singh Nagar	4	0
13	Uttarkashi	70	0

4. Program Workstream Progress

Outreach and Mobilisation

S.No.	Indicator	Achievement
1.1	Call for Application	909
1.2	District Level Workshops	3
1.3	No. of Awareness cum Outreach activities for SHG members/Potential Lakhpati Didis/ SHGs/CBOs etc.	24
1.3.1	Participants in Awareness cum Outreach activities	574
1.4	EAP/EDP Sessions	12

Identification and Onboarding of Enterprises

No approved achievement was recorded for this workstream during August 2026.

Training & Capacity Building

S.No.	Indicator	Achievement
3.1	Business Skills Training Sessions	7
3.2	Incubatees taken Part in Business Modules Training	212
3.3.1	Technical Trainings to Potential Lakhpati Didis/ SHG Members/ CBOs	1

Business Formalization

S.No.	Indicator	Achievement
4.1.1	Business Registration	74
4.2.1	Artisan Card	8
4.2.2	FSSAI	14
4.2.3	UTDB	1
4.2.4	GST Registration	4
4.2.5	Trademark application filling	1
4.2.7	Advance Licensing Support (Mandi Licensing, Lab Test etc.)	1

Mentorship

S.No.	Indicator	Achievement
5.1	Specialized Mentorship Support	25

Partnership & Forward Linkages

S.No.	Indicator	Achievement
6.1	No of Partners outreach	11
6.3	Incubatees linked to online/offline Market	15

Business Acceleration Services

S.No.	Indicator	Achievement
7.2	Initiation of acceleration and co-incubation services	15

Funding & Schematic Convergence

S.No.	Indicator	Achievement
-------	-----------	-------------

S.No.	Indicator	Achievement
8.1	Schematic Convergence	48
8.2	Support to MUY Incubatee through Reap	4

Other Support Services

S.No.	Indicator	Achievement
9.1	Business Model Canvas	185
9.2	Other Support Services - Labelling, Packaging, Logo Designing etc.	2

Branding, Communication & Knowledge Management

S.No.	Indicator	Achievement
10.1	Social Media Post	3
10.2	Preparation of Case Studies and Testimonials	1

Product Development

No approved achievement was recorded for this workstream during August 2026.

Synergies Across Line Departments

S.No.	Indicator	Achievement
12.2	Meeting of staff with Line Department at Spoke/Hub/State Level	1

5. Field Highlights

Approved field photographs available in the MIS Media Gallery for the reporting month.




Block Workshops - Dasholi
Chamoli | 16 Aug 2026



Block Workshops - Narayanbagar
Chamoli | 13 Aug 2026



District Workshops - District workshop
Rudraprayag | 05 Aug 2026

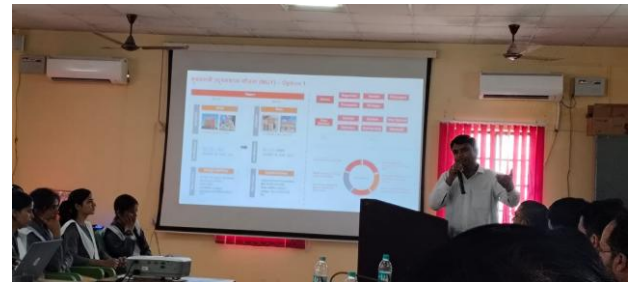

District Workshops - District workshop
Pauri Garhwal | 05 Aug 2026



EAP / EDP Sessions - EAP/EDP session
Pauri Garhwal | 17 Aug 2026



EAP / EDP Sessions - EAP/EDP session
Tehri Garhwal | 14 Aug 2026



Lakhpatri Technical Trainings - Importance of Social Media Management in collaboration with Upliftlive Foundation
Pauri Garhwal | 07 Aug 2026



Line Department Meetings - Education
— | 17 Aug 2026

6. Report Basis and Data Notes

Reporting period: 01 Aug 2026 to 31 Aug 2026.

Fiscal year: FY 2026-27.

Achievements are generated from approved MIS records and the existing MUY deliverables reporting logic.

Cumulative values cover the start of the fiscal year through the end of the selected month.

Field photographs are selected from Media Gallery records that satisfy the module visibility and approval rules.

A zero indicates that no qualifying approved record was found under the applicable MIS logic; it does not replace independent program validation.

Report generated on 18 Aug 2026, 12:23 PM.

Thank You

This report is generated from the MUY MIS for the selected reporting month and is intended for programme review.

The document should be reviewed by the State Project Management Unit before external circulation.

The report may contain forward-looking actions and operational observations that remain subject to validation.
